



FLOODLIGHT UPGRADE PROJECT

Courts 1 to 6

(Sept 2016 – Dec 2016)




Attaching the LED light bank to the pole



Carefully maneuvering the pole into position



Sorting out the cabling & LED driver in the Pole

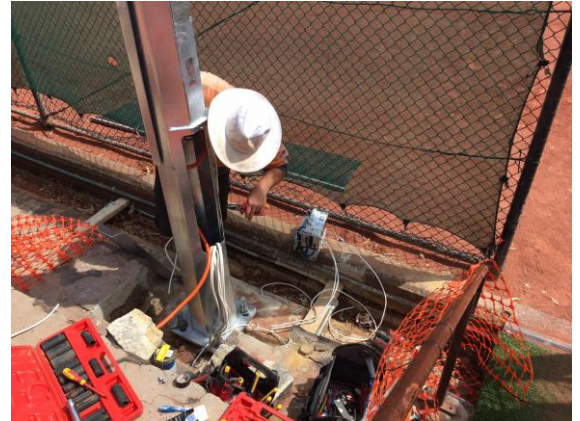

<p>WHAT HAVE WE DONE TO DATE</p>	<p>Met onsite a number of times with City of Stonnington Project Manager and Commlec Project Manager. Service detection carried out around planned cable locations. Trenching for electrical cables done. Horizontal drilling where required for cabling. Concrete footings for 8 poles. Cabling to switch box. Poles ordered.</p>
<p>WHAT ARE WE DOING NOW (28 Nov – 02 Dec 2016)</p>	<p>Poles & LED fittings delivered and erected. All wiring ready for connection & testing.</p>
<p>WHAT ARE WE DOING NEXT (05 - 09 December 2016)</p>	<p>Final testing & commissioning of new lights to take place. Old lights will be disconnected at the same time as the switches remain the same. Old lights to be decommissioned and removed from sight (this may not be done immediately).</p>
<p><i>THINGS TO NOTE</i></p>	<p><i>The existing floodlights will remain operational throughout the whole process and only be removed once then new LED floodlights have been commissioned and are ready to go.</i></p>
